


NCDOT
Division 6
Harnett County
Project Report
January 2026



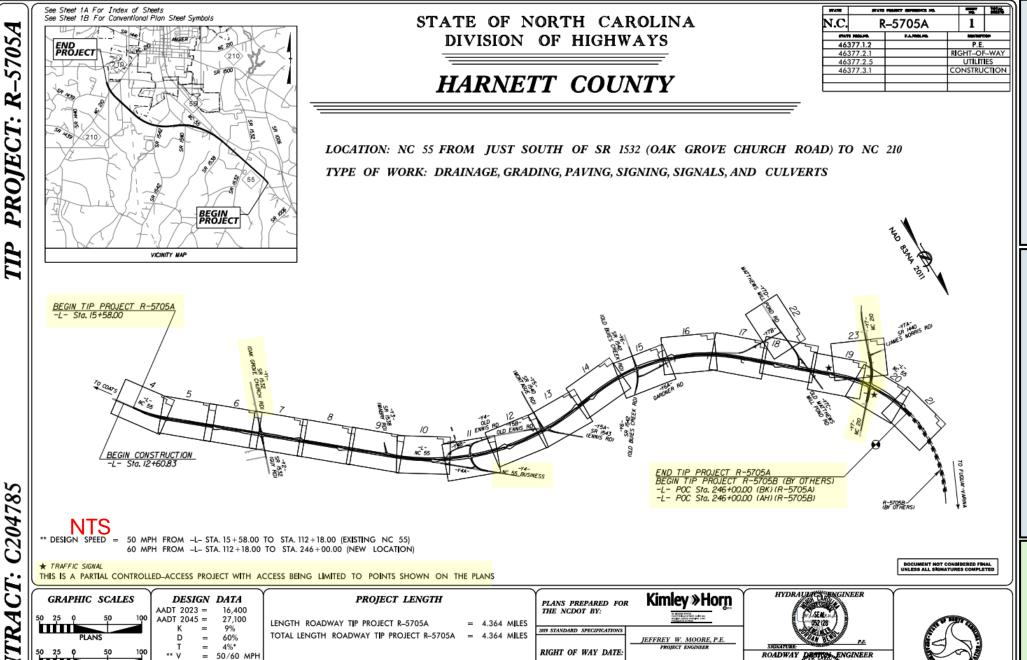

MARCH 9, 2021

LETTING DATE:

SEPTEMBER 19, 2023

EVERETT J. LOVING, P.E.

DAVID WERR P.F.

(TTST 1% + DUAL 3%)

FUNCTIONAL

CLASSIFICATION:

MINOR ARTERIAL

REGIONAL TIER

PROFILE (HORIZONTAL)

PROFILE (VERTICAL)

Project Details:

Work Begin: 12/2023

Est. Completion: 04/2028

Rev. Completion: N/A

Contractor: Barnhill

NCDOT Contact: Donavon Hunt

Contract: \$48,441,331


Project Comments:

Majority of project is located on new alignment.

CONSTRUCTION PROGRESS

35%

11/15/2025

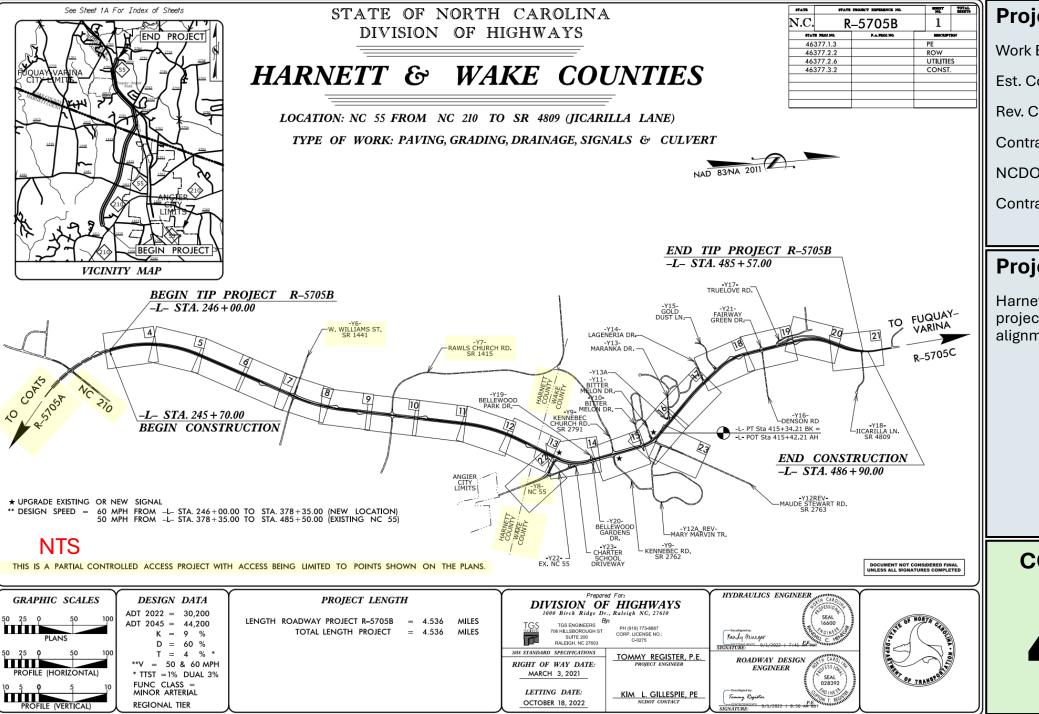

-5705B

×

PROJECT:

C204745

Project Details:

Work Begin: 03/2023

Est. Completion: 05/2027

Rev. Completion: 10/2027

Contractor: Highland Paving

NCDOT Contact: Donavon Hunt

Contract: \$61,497,777


Project Comments:

Harnett County portion of project is located on new alignment.

CONSTRUCTION PROGRESS

47%

11/30/2025

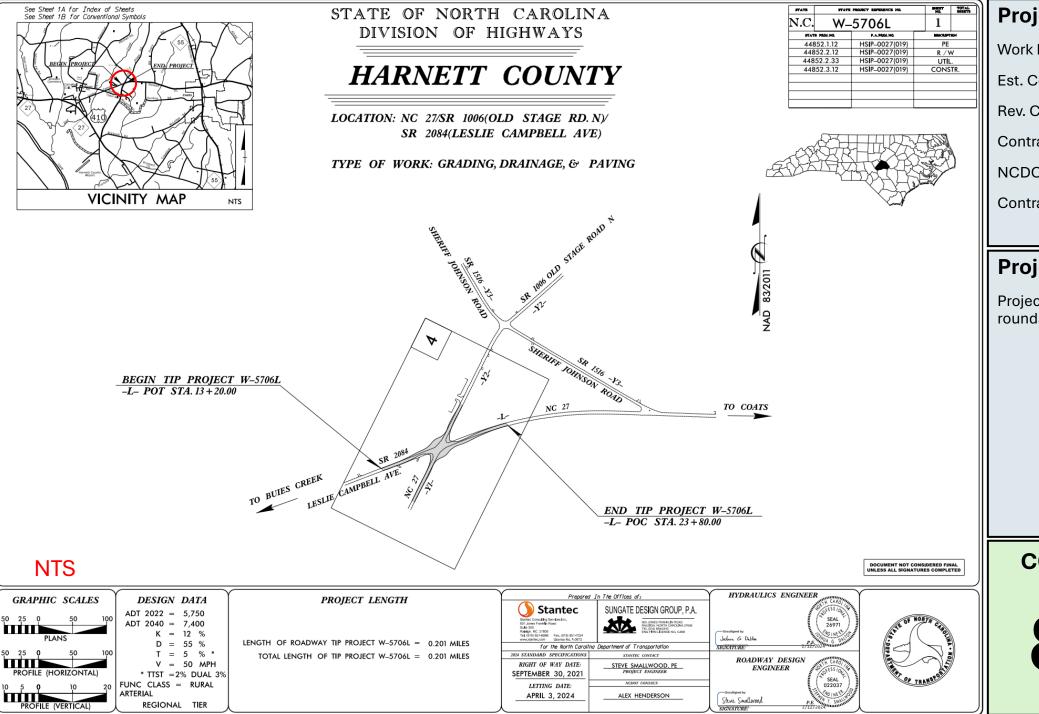

W-5706L

PROJECT:

DF00465

Project Details:

Work Begin: 09/2024

Est. Completion: 12/2025

Rev. Completion: 03/2026

Contractor: Highland Paving

NCDOT Contact: Donavon Hunt

Contract: \$2,708,263


Project Comments:

Project will construct a roundabout.

CONSTRUCTION PROGRESS

81%

10/13/2025

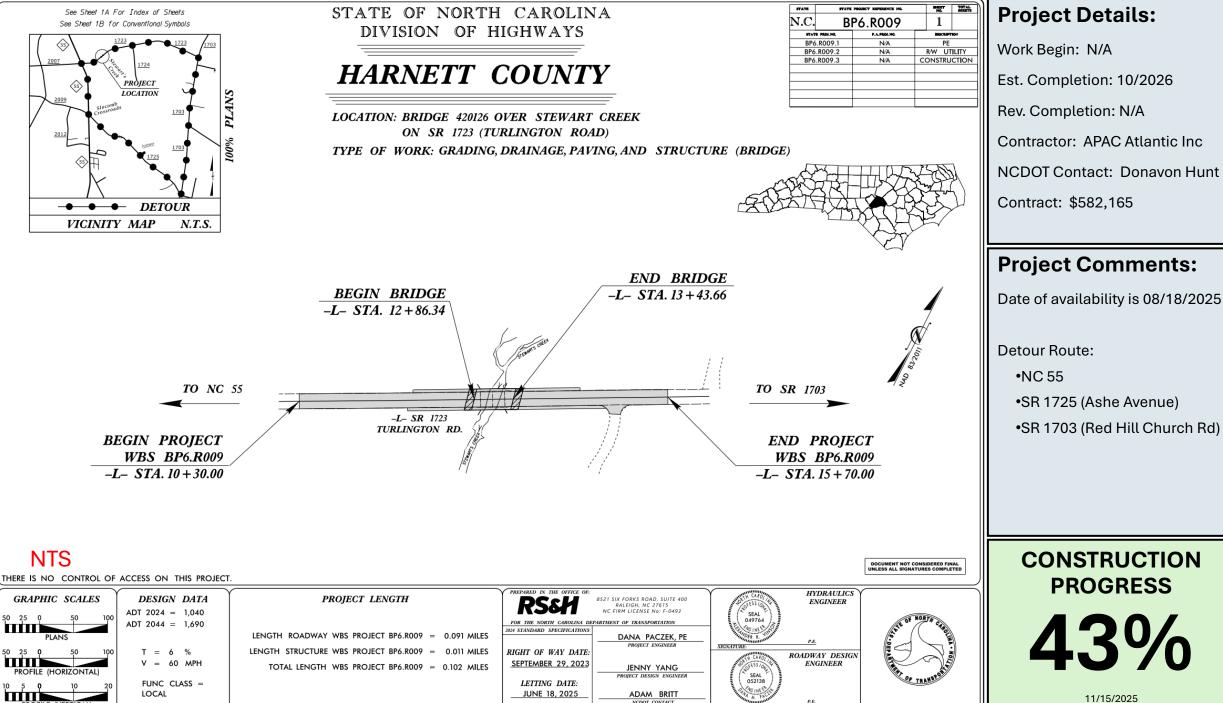

BP6.R009

WBS:

DF00503

Est. Completion: 10/2026

Contractor: APAC Atlantic Inc


NCDOT Contact: Donavon Hunt

Project Comments:

CONSTRUCTION **PROGRESS**

43%

11/15/2025

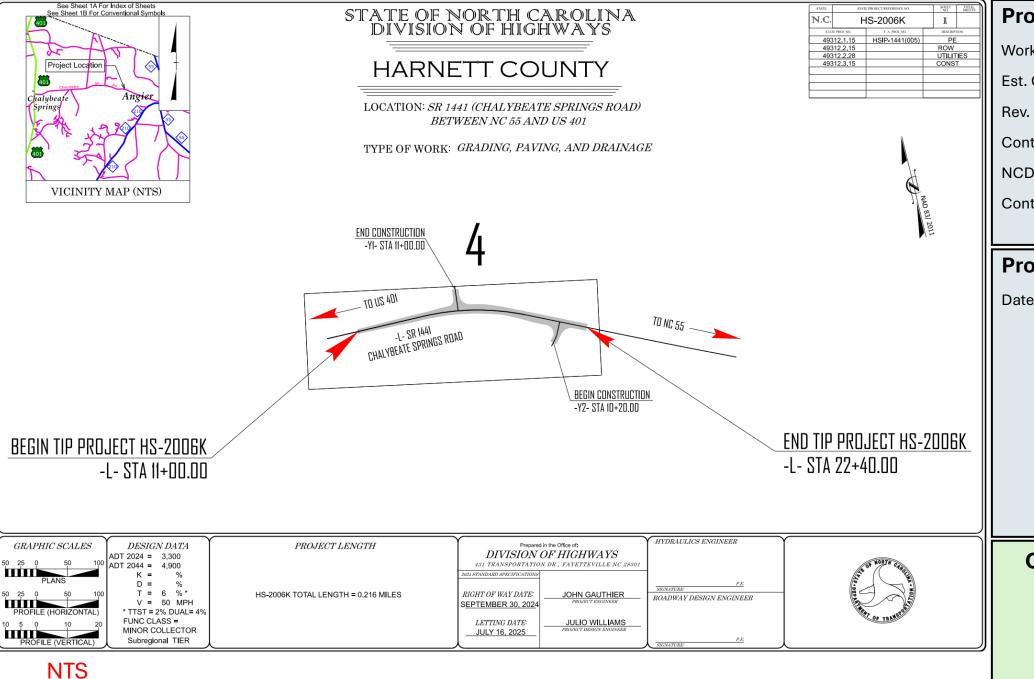

Project Details:

Work Begin: 09/2025

Est. Completion: 06/2026

Rev. Completion: N/A

Contractor: Highland Paving

NCDOT Contact: Donavon Hunt

Contract: \$692,317

Project Comments:

Date of availability is 08/18/2025

CONSTRUCTION **PROGRESS**

12/03/2025

HS-2006K

TIP PROJECT:

DF00519

NCDOT, Div. 6 HMIP (Active Project)

| Contract | Project | Contractor | Let | Completion | Progress | Cost | County |
|----------|--|---|---------|------------|--------------------------|-------------|--|
| DF00441 | Concrete installations in Division 6 (curb ramps) | Morgan Trucking & GC | 09/2023 | 10/2025 | 82% 09/07/2025 | \$2,530,730 | Bladen, Cumberland, Harnett, & Robeson |
| DF00475 | Resurfacing, milling, & pavement markings along 20 SR's totaling 22.08 miles | Highland Paving | 04/2024 | 10/2025 | 83% 10/31/2025 | \$3,178,982 | Harnett |
| DF00493 | Concrete installations. | Eastern Earthscapes & Construction LLC | 09/2024 | 10/2026 | 39% 10/22/2025 | \$688,923 | Bladen, Columbus, Cumberland, Harnett & Robeson |
| DF00499 | Widening, resurfacing & pavement markings along 11 SR's totaling 20.33 miles | Fred Smith Co. | 10/2024 | 04/2026 | 79% 08/31/2025 | \$2,841,205 | Harnett |
| DF00515 | Resurfacing, widening, milling, & pavement markings (Various routes; includes (S.10th St.) & SR 1542 within CAMPO Boundary | Johnson Brothers | 04/2025 | 11/2026 | 0 % 10/24/2025 | \$2,581,068 | Harnett |
| DF00533 | Widening, resurfacing, milling, & pavement markings (NC 27, SR 1700 (Cane Mill Road), & SR 1705 (Fairground Road) in CAMPO | Johnson Brothers | 11/2025 | 06/2027 | 0% 10/24/2025 | \$1,873,101 | Harnett |

Boundary

Note: Projects details are subject to change

NCDOT, Division 6 – Future Projects

| TIP/WBS | County | Project | R/W | Let | Est. Project Cost |
|---------|---------|--|---------|---------|-------------------|
| EB-6020 | Harnett | Sidewalk extensions along: N . Willow Street, b/w E. Julia Street and SR 1500 (Junny Road) SR 1500 (Junny Road), b/w N. Willow Street and Glen Meadow Drive W. Lillington Street, b/w S. Park Street and NC 210 | 10/2024 | 09/2025 | \$1,782,000 |
| BL-0090 | Harnett | SR 1500 (E. McIver Street), b/w Angier Elementary School and S. Wilma Street (ss) & S. Wilma Street, b/w SR 1500 and approx. 700' south of SR 1500 (ws) - Sidewalk | 2025 | 09/2026 | \$1,098,000 |
| R-5890 | Harnett | US 401 (North Main Street) from Parker Lane to McKinney Parkway – construct median and traffic signal | TBD | TBD | \$16,210,000 |



Philip Hart, NCDOT Division 6 Planning Engineer

Email: pjhart@ncdot.gov Phone: 910-364-0022
