


NCDOT
Division 6
Harnett County
Project Report
June 2025



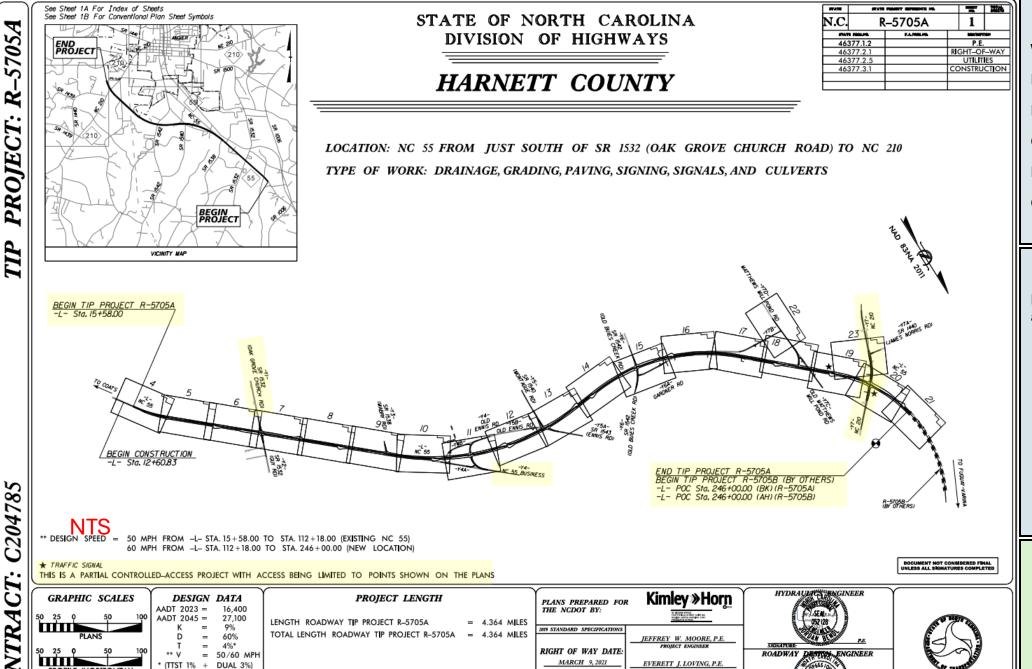

LETTING DATE:

SEPTEMBER 19, 2023

DAVID WERR P.F.

PROFILE (HORIZONTAL)

PROFILE (VERTICAL)

FUNCTIONAL

CLASSIFICATION:

MINOR ARTERIAL

REGIONAL TIER

Project Details:

Work Begin: 12/2023

Est. Completion: 04/2028

Rev. Completion: N/A

Contractor: Barnhill

NCDOT Contact: Donavon Hunt

Contract: \$48,441,331

Project Comments:


Majority of project is on new alignment.

CONSTRUCTION

30%

04/15/2025

PROGRESS

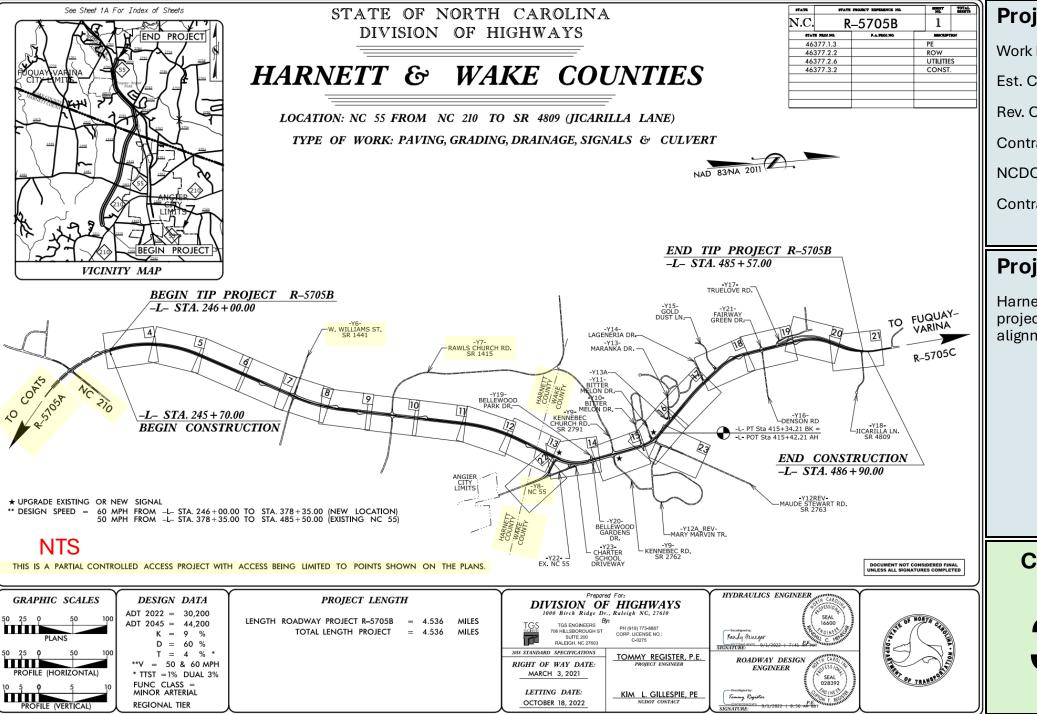

-5705B

2

PROJECT:

C204745

Project Details:

Work Begin: 03/2023

Est. Completion: 05/2027

Rev. Completion: 10/2027

Contractor: Highland Paving

NCDOT Contact: Donavon Hunt

Contract: \$61,497,777


Project Comments:

Harnett County portion of project is located on new alignment.

CONSTRUCTION PROGRESS

36%

03/31/2025

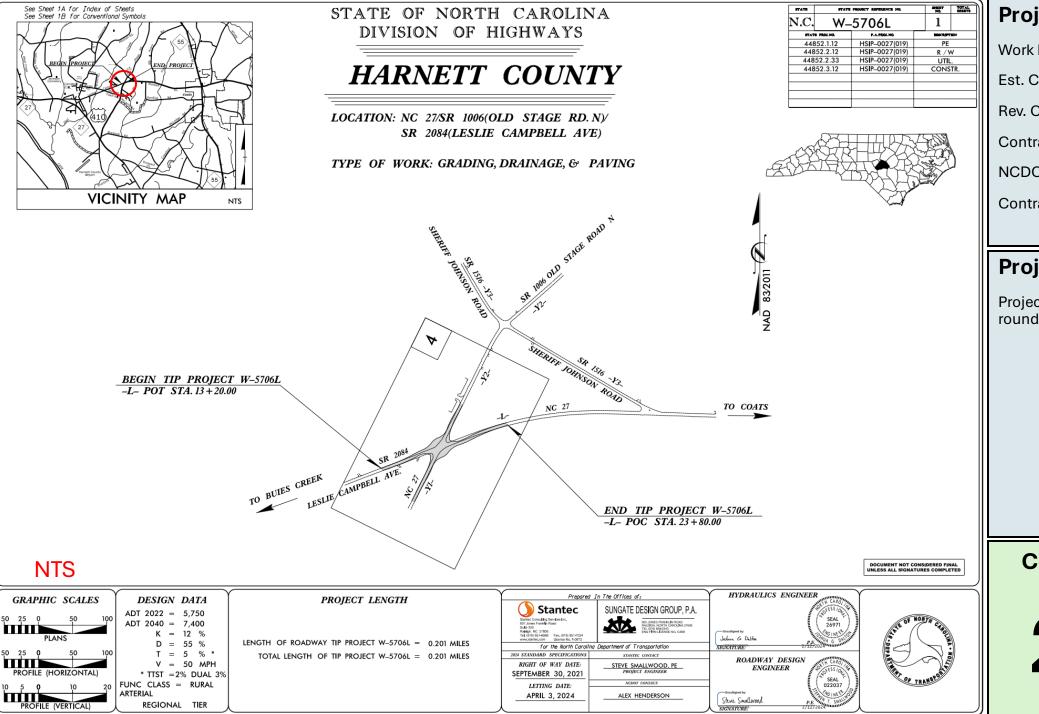

W-5706L

PROJECT:

DF00465

Project Details:

Work Begin: 09/2024

Est. Completion: 12/2025

Rev. Completion: 02/2026

Contractor: Highland Paving

NCDOT Contact: Donavon Hunt

Contract: \$2,708,263

Project Comments:

Project will construct a roundabout.

CONSTRUCTION PROGRESS

23%

04/07/2025

NCDOT, Div. 6 HMIP (Active Project)

Let

Completion

Progress

Cost

County

Contractor

Project

St.) & SR 1542 within CAMPO Boundary

Contract

				5 5 5 5 p			,
DF00441	Concrete installations in Division 6 (curb ramps)	Morgan Trucking & GC	09/2023	10/2025	71% 05/07/2025	\$2,530,730	Bladen, Cumberland, Harnett, & Robeson
DF00442	Resurfacing, widening, milling, & pavement markings along 10 SR's totaling 22.93 miles.	Johnson Brothers	06/2023	10/2024	95% 04/30/2025	\$4,132,586	Harnett
DF00470	Widening, milled rumble stripes & pavement markings	Performance Sealing & Striping	03/2024	04/2025	81% 01/15/2025	\$1,927,560	Bladen, Cumberland, Harnett, & Robeson
DF00475	Resurfacing, milling, & pavement markings along 20 SR's totaling 22.08 miles	Highland Paving	04/2024	10/2025	24 % 04/30/2025	\$3,178,982	Harnett
DF00476	Resurfacing, milling, & pavement markings along 40 SR's totaling 25.96 miles	Fred Smith Co.	04/2024	11/2025	94% 04/30/2025	\$3,446,744	Harnett
DF00479	AST (double seals, joint sealer & pav't mrkgs.) along 20 SR's totaling 31.66 miles	Whitehurst Paving Co.	07/2024	06/2025	5% 08/31/2024	\$1,181,086	Harnett
DF00493	Concrete installations.	Eastern Earthscapes & Construction LLC	09/2024	10/2026	0 % 05/20/2025	\$688,923	Bladen, Columbus, Cumberland, Harnett & Robeson
DF00499	Widening, resurfacing & pavement markings along 11 SR's totaling 20.33 miles	Fred Smith Co.	10/2024	04/2026	0 % 05/20/2025	\$2,841,205	Harnett
DF00510	Permanent raised pavement marker installations along 1,195 miles of roadways	McCain Striping Service, Inc.	03/2025	10/2025	10% 04/22/2025	\$531,589	Bladen, Columbus, Cumberland, Harnett, & Robeson
DF00515	Resurfacing, Widening, Milling, & Pavement Markings (Various routes including (S.10th	Johnson Brothers	04/2025	11/2026	0 % 05/20/2025	\$2,581,068	Harnett

Note: Projects details are subject to change

NCDOT, Division 6 – STIP (Future)											
TIP/WBS	County	Project		Let	Est. Project Cost						
R-5890	Harnett	US 401 (North Main Street) from Parker Lane to McKinney Parkway – construct median and traffic signal	06/2029	01/2031	\$17,410,000						
R-5953	Harnett	NC 55 from NC 27 in Coats to Old Stage Road – widen existing & construct new alignment	TBD	TBD	\$85,500,000						
NCDOT, Division 6 – Bridge (Future)											
TIP/WBS	County	Project	R/W	Let	Est. Project Cost						
BP6.R009	Harnett	SR 1723 (Turlington Road) Bridge # 420126 replacement over Stewart Creek	10/2023	06/2025	\$1,380,000						
NCDOT, Division 6 - Safety (Future)											
TIP/WBS	County	Project	R/W	Let	Est. Project Cost						
HS-2006K	Harnett	SR 1441 (Chalybeate Springs Road) between NC 55 and US 401 – wedge curve near Wells Lane; place long life pavement markings (LLPM) on entire route	09/2024	07/2025	\$1,345,000						
NCDOT, Division 6 - LAP (Future)											
TIP/WBS	County	Project	R/W	Let	Est. Project Cost						
BL-0090	Harnett	SR 1500 (E. McIver Street), b/w Angier Elementary School and S. Wilma Street (ss) & S. Wilma Street, b/w SR 1500 and approx. 700' south of SR 1500 (ws) - Sidewalk	2025	06/2025	\$1,098,000						
EB-6020	Harnett Sidewalk extensions along: N. Willow Street, b/w E. Julia Street and SR 1500 (Junny Road) SR 1500 (Junny Road), b/w N. Willow Street and Glen Meadow Drive W. Lillington Street, b/w S. Park Street and NC 210		10/2024	08/2025	\$1,782,000						
