


NCDOT
Division 6
Harnett County
Project Report
September 2025



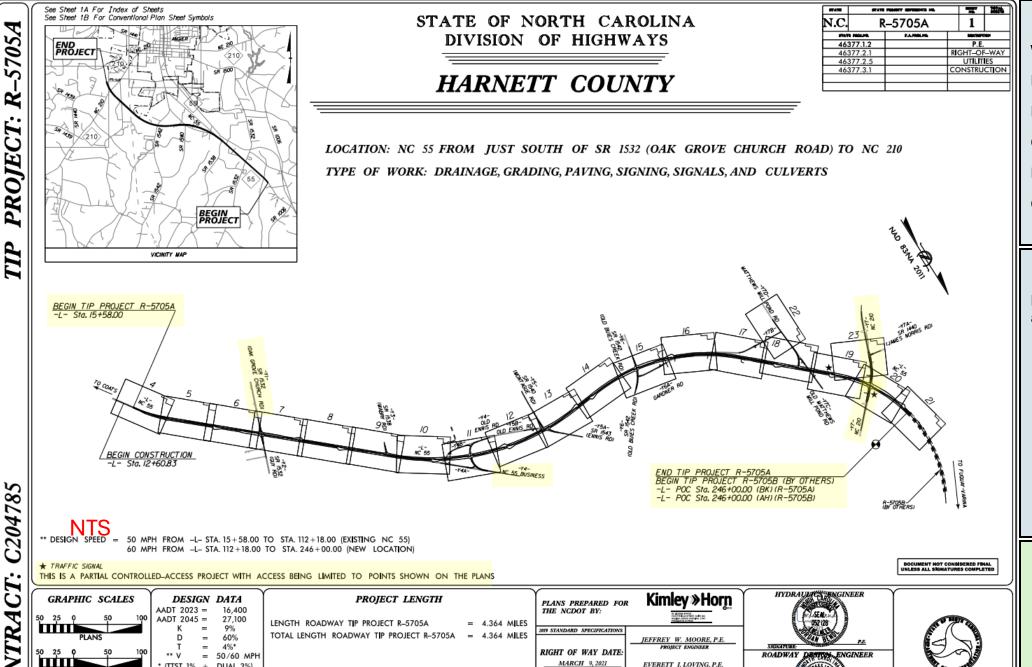

EVERETT J. LOVING, P.E.

DAVID WERR P.F.

LETTING DATE:

SEPTEMBER 19, 2023

(TTST 1% + DUAL 3%)

FUNCTIONAL

CLASSIFICATION:

MINOR ARTERIAL

REGIONAL TIER

PROFILE (HORIZONTAL)

PROFILE (VERTICAL)

Project Details:

Work Begin: 12/2023

Est. Completion: 04/2028

Rev. Completion: N/A

Contractor: Barnhill

NCDOT Contact: Donavon Hunt

Contract: \$48,441,331


Project Comments:

Majority of project is on new alignment.

CONSTRUCTION **PROGRESS**

33%

07/15/2025

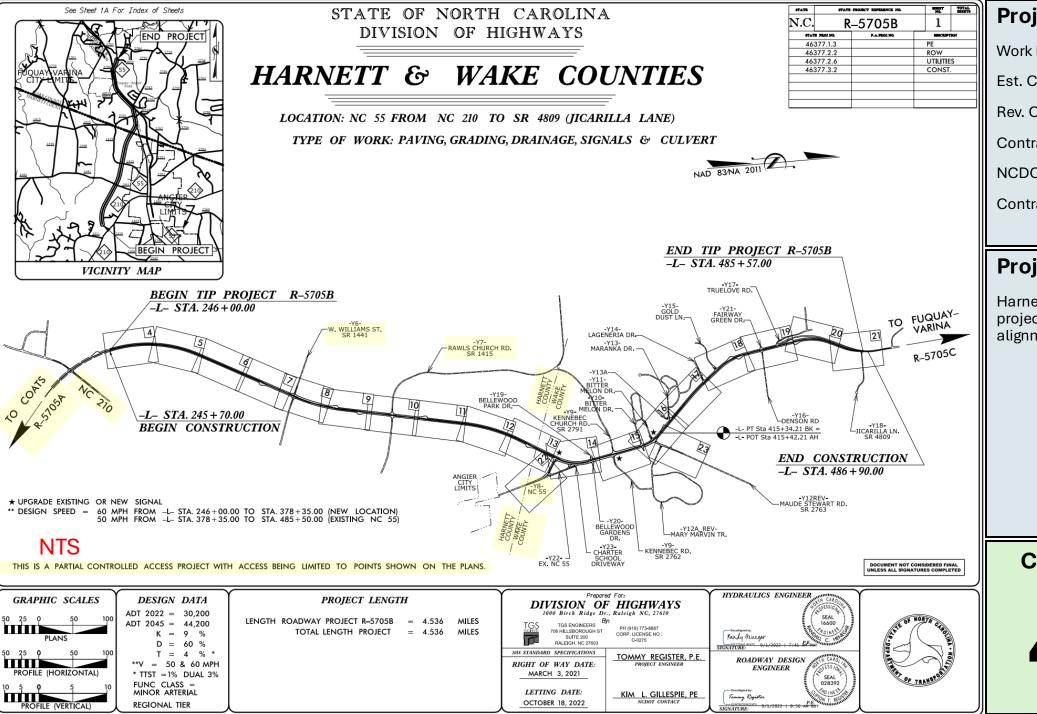

-5705B

2

PROJECT:

C204745

Project Details:

Work Begin: 03/2023

Est. Completion: 05/2027

Rev. Completion: 10/2027

Contractor: Highland Paving

NCDOT Contact: Donavon Hunt

Contract: \$61,497,777


Project Comments:

Harnett County portion of project is located on new alignment.

CONSTRUCTION PROGRESS

44%

07/31/2025

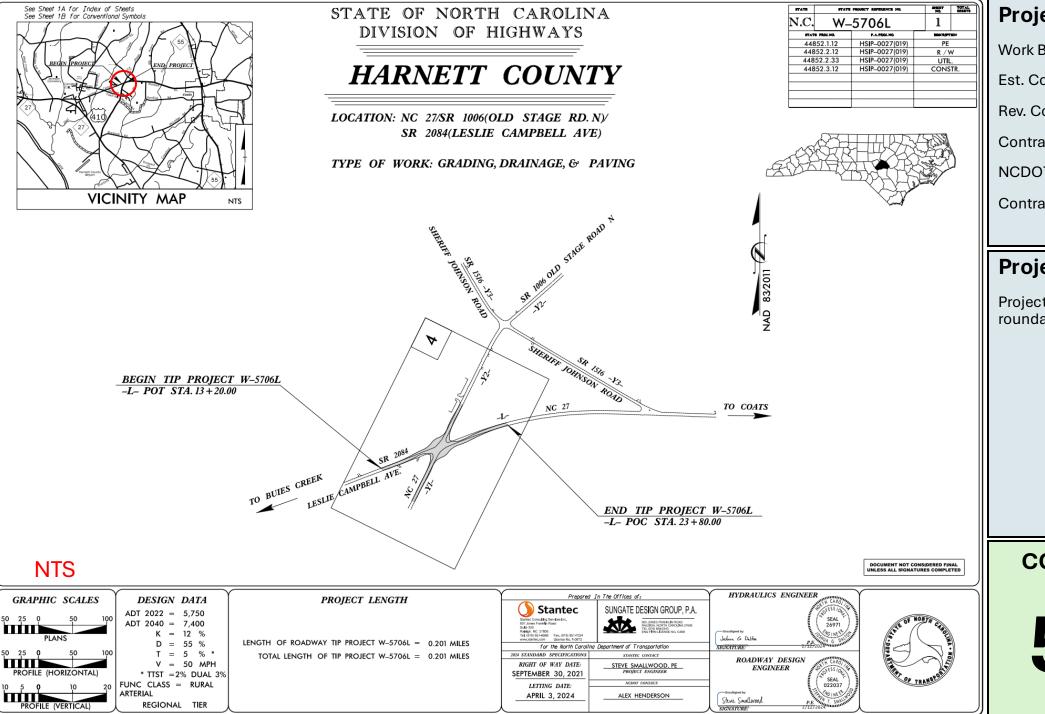

W-5706L

PROJECT:

DF00465

Project Details:

Work Begin: 09/2024

Est. Completion: 12/2025

Rev. Completion: 02/2026

Contractor: Highland Paving

NCDOT Contact: Donavon Hunt

Contract: \$2,708,263


Project Comments:


Project will construct a roundabout.

CONSTRUCTION PROGRESS

52%

07/07/2025

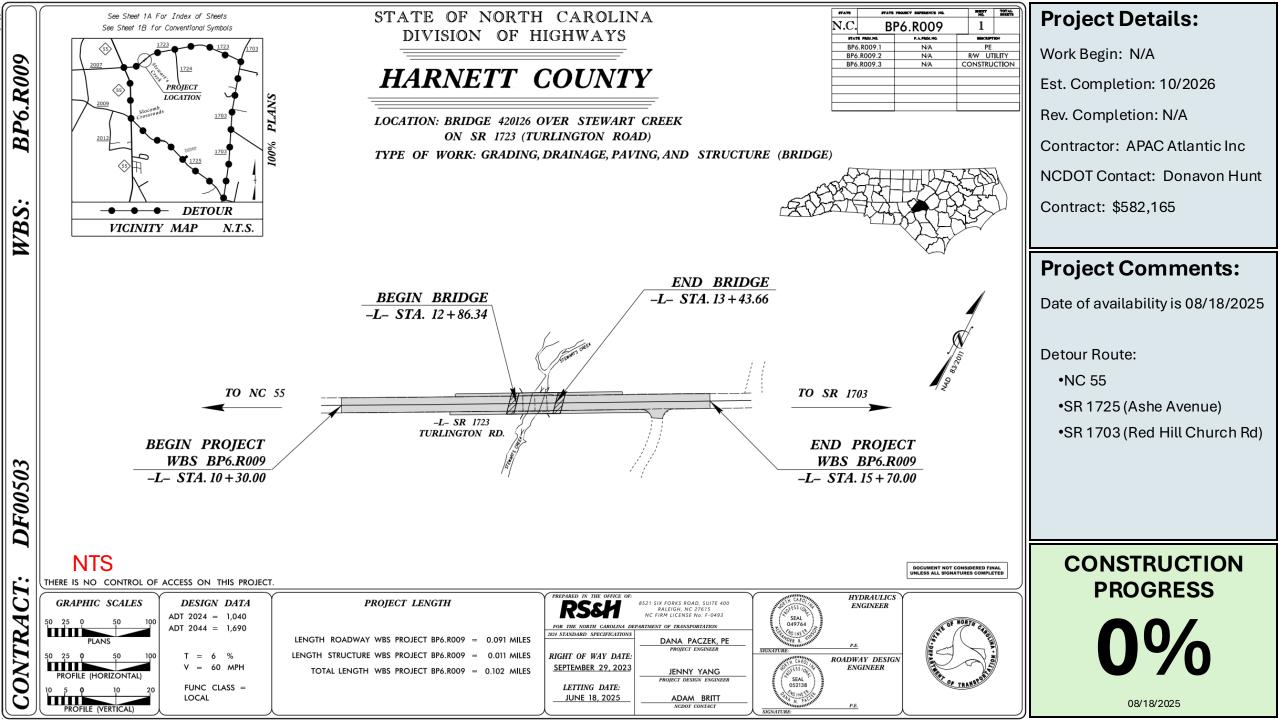

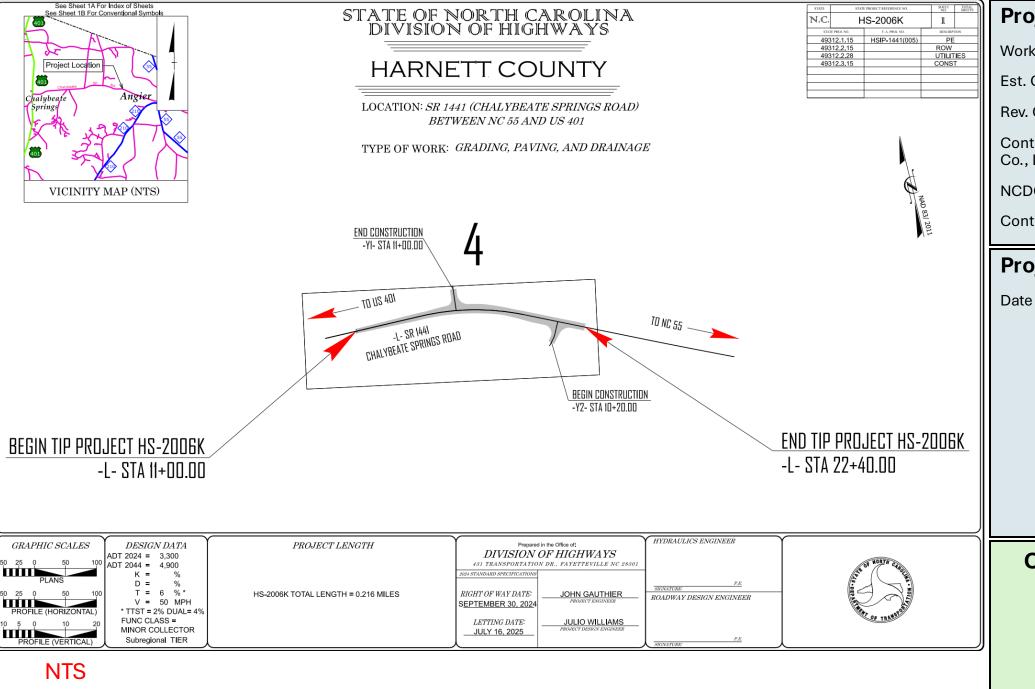

HS-2006K

TIP PROJECT:

Project Details:

Work Begin: N/A

Est. Completion: 06/2026

Rev. Completion: N/A

Contractor: Highland Paving

Co., LLC

NCDOT Contact: Donavon Hunt

Contract: \$692,317

Project Comments:

Date of availability is 08/18/2025

CONSTRUCTION PROGRESS

08/18/2025

NCDOT, Div. 6 HMIP (Active Project)

Contract	Project	Contractor	Let	Completion	Progress	Cost	County
DF00441	Concrete installations in Division 6 (curb ramps)	Morgan Trucking & GC	09/2023	10/2025	77% 07/07/2025	\$2,530,730	Bladen, Cumberland, Harnett, & Robeson
DF00475	Resurfacing, milling, & pavement markings along 20 SR's totaling 22.08 miles	Highland Paving	04/2024	10/2025	41% 06/30/2025	\$3,178,982	Harnett
DF00493	Concrete installations.	Eastern Earthscapes & Construction LLC	09/2024	10/2026	16% 07/22/2025	\$688,923	Bladen, Columbus, Cumberland, Harnett & Robeson
DF00499	Widening, resurfacing & pavement markings along 11 SR's totaling 20.33 miles	Fred Smith Co.	10/2024	04/2026	73% 07/31/2025	\$2,841,205	Harnett
DF00510	Permanent raised pavement marker installations along 1,195 miles of roadways	McCain Striping Service, Inc.	03/2025	10/2025	50 % 07/22/2025	\$531,589	Bladen, Columbus, Cumberland, Harnett, & Robeson
DF00515	Resurfacing, Widening, Milling, & Pavement Markings (Various routes including (S.10th St.) & SR 1542 within CAMPO Boundary	Johnson Brothers	04/2025	11/2026	0 % 08/18/2025	\$2,581,068	Harnett

NCDOT, Division 6 – STIP (Future)

TIP/WBS	County	Project	R/W	Let	Est. Project Cost
R-5890	Harnett	US 401 (North Main Street) from Parker Lane to McKinney Parkway – construct median and traffic signal	06/2029	01/2031	\$17,410,000
R-5953	Harnett	NC 55 from NC 27 in Coats to Old Stage Road – widen existing & construct new alignment	TBD	TBD	\$85,500,000

NCDOT, Division 6 - LAP (Future)

TIP/WBS	County	Project	R/W	Let	Est. Project Cost
BL-0090	Harnett	SR 1500 (E. McIver Street), b/w Angier Elementary School and S. Wilma Street (ss) & S. Wilma Street, b/w SR 1500 and approx. 700' south of SR 1500 (ws) - Sidewalk	2025	09/2026	\$1,098,000
EB-6020	Harnett	 Sidewalk extensions along: N . Willow Street, b/w E. Julia Street and SR 1500 (Junny Road) SR 1500 (Junny Road), b/w N. Willow Street and Glen Meadow Drive W. Lillington Street, b/w S. Park Street and NC 210 	10/2024	09/2025	\$1,782,000



Philip Hart, NCDOT Division 6 Planning Engineer
Email: pjhart@ncdot.gov Phone: 910-364-0022
