



NORTH CAROLINA

Department of Transportation



October 2021 Project Update
U-2719 I-440
U-4437 Blue Ridge Rd/Hillsborough St.

Brandon Jones, Division Five Engineer



Oldest Section of I-440

Design Build Contract
Awarded to Lane
Construction/HDR in October
2018 - \$346.2M

Work Began in July 2019

Widening from 4 to 6 lanes

Replacing Pavement

Replacing Bridges

Upgrading Interchanges



Wade Avenue





Wade Avenue



I440 Raleigh Beltline

7-31-21

Wade Avenue



Wade Avenue






Wade Avenue



Hillsborough Street

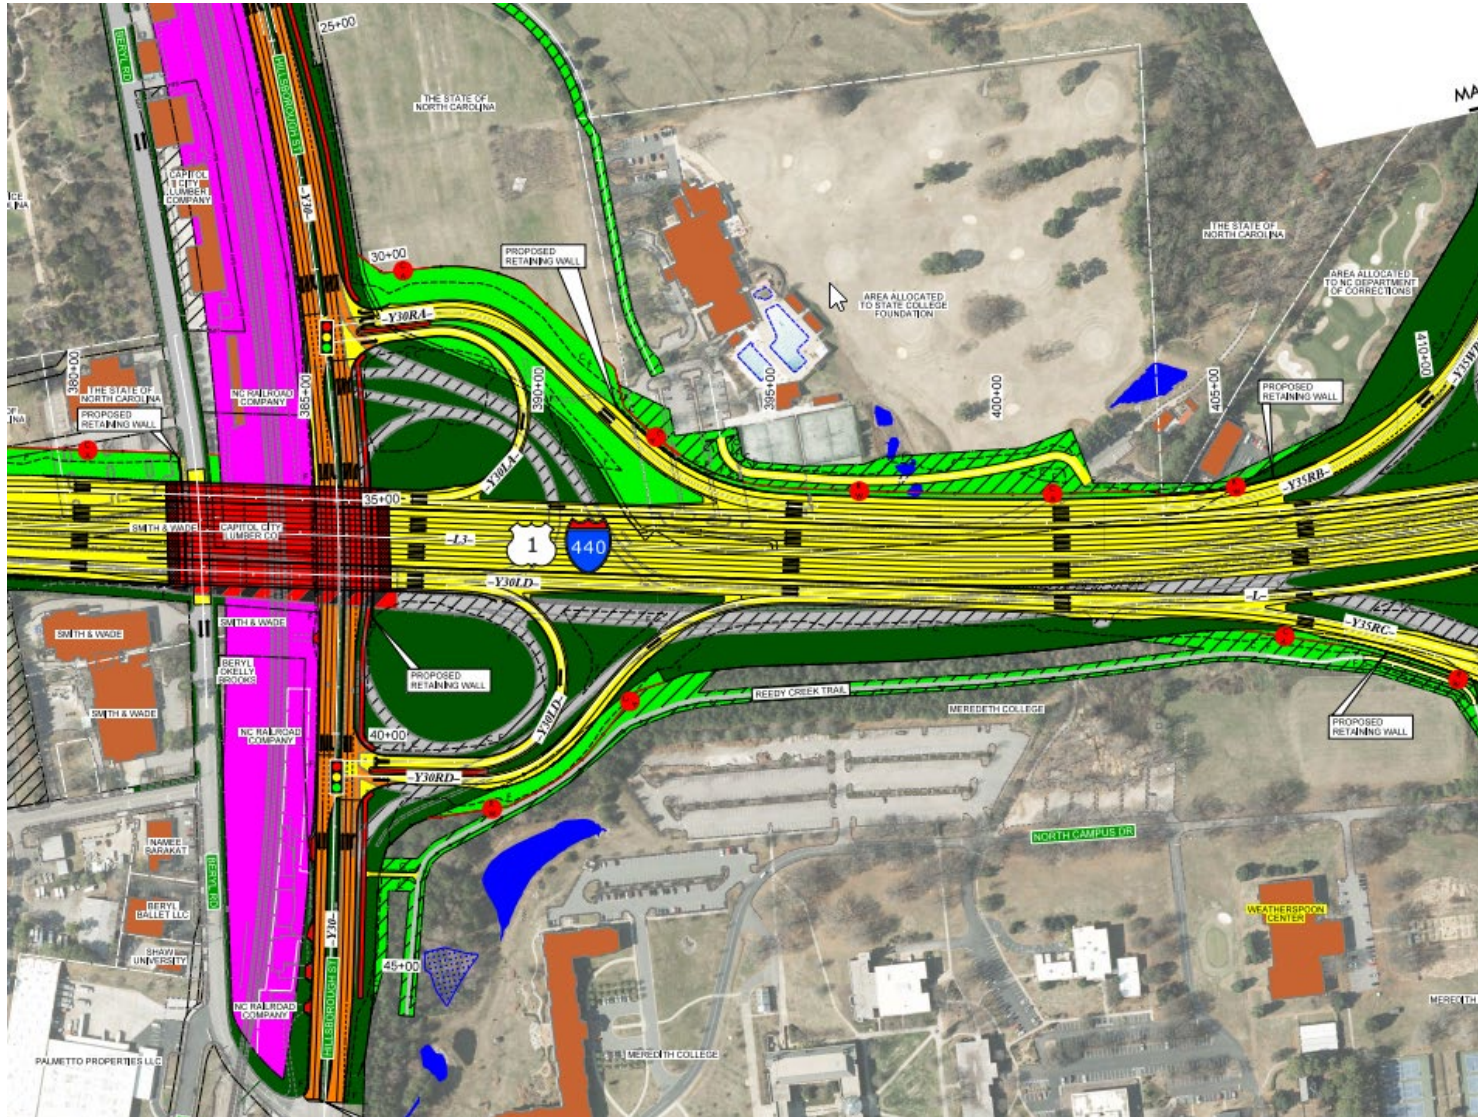



Hillsborough Street



Hillsborough Street



Western Boulevard




Western Boulevard





Western Boulevard

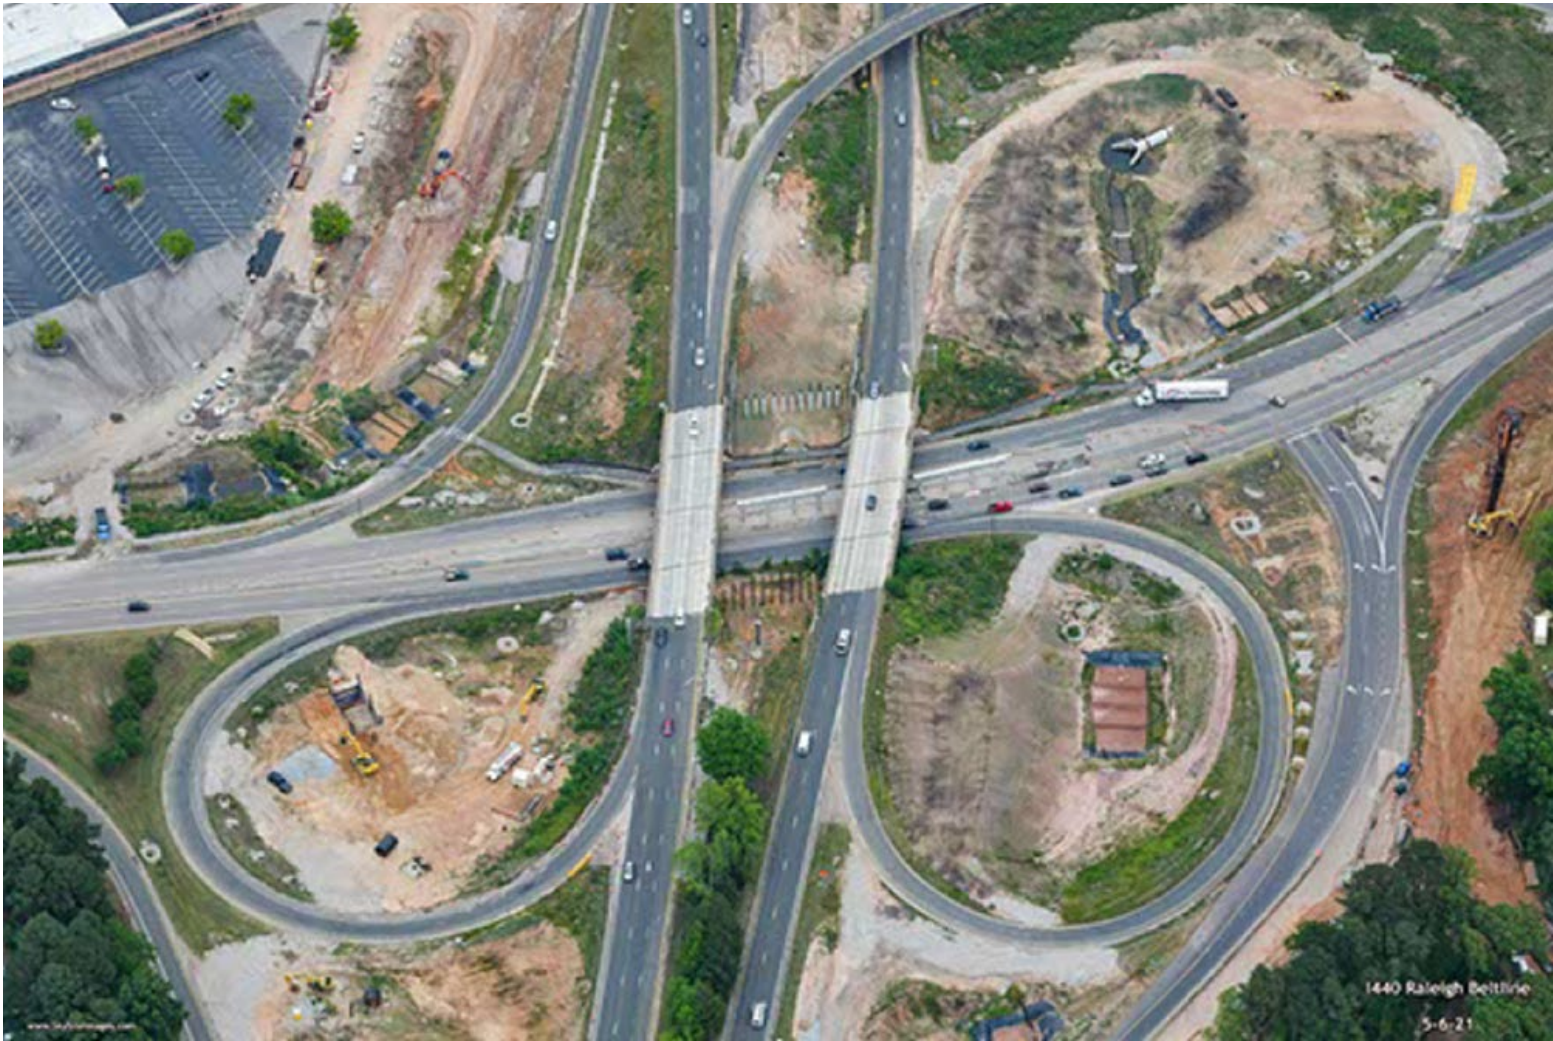



Western Boulevard





Melbourne Road






Athens Drive



Jones Franklin Road

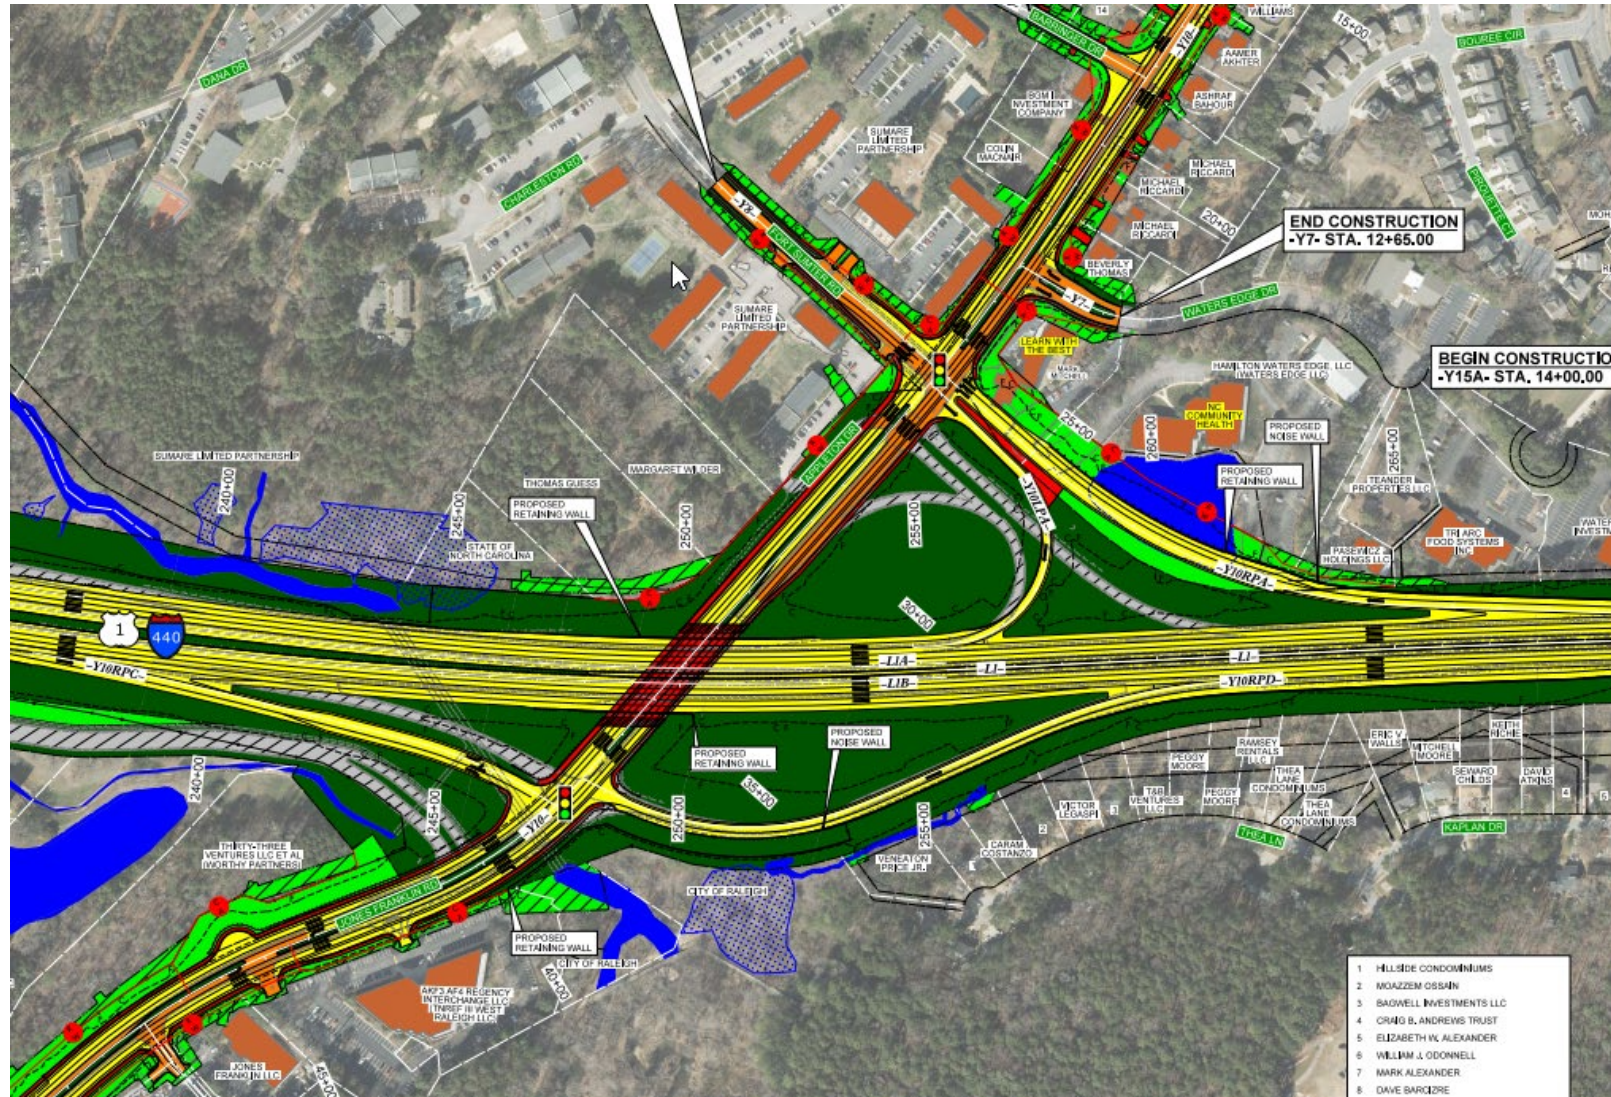



Jones Franklin Road



U-2719 I-440 Next Steps

Shift to New Ramp D at Wade – Completed

Shift to Temporary Median between Melbourne and Athens – Completed

Shift to New Loop C at Wade – Completed

Shift Mainline to new structure 3 (I-440 over Wade) – October 2021

Closure at Athens Drive – November 2021

Closures and shifts at Western – October/November 2021

- DDI Completion – February 2023

Shift to New Bridge at Jones Franklin – January 2022





U-4437 Blue Ridge Road/Hillsborough Street Grade Separation





U-4437 Blue Ridge Road/Hillsborough Street Grade Separation

View West





U-4437 Blue Ridge Road/Hillsborough Street Grade Separation – Next Steps

View West

Closure of Blue Ridge – 11/1/2021 – 10/1/2023

Closure of Hillsborough – Early 2022 – Mid 2022

